

9172.00 IVH-Loftus 2nd Floor Remodel		DCI - Update	
#	Activity Name	Remaining Duration	
1	9172.00 IVH-Loftus 2nd Floor Remodel		
2	Milestones		
3	Preconstruction		
4	RFP Procurement	13	■ RFP Procurement
5	Hazardous Materials Contract	5	■ Hazardous Materials Contract
6	Design RFP Pre-Proposal	1	■ Design RFP Pre-Proposal
7	Hazardous Materials Investigation	2	■ Hazardous Materials Investigation
8	Hazardous Materials Final Report	10	■ Hazardous Materials Final Report
9	RFPs Due	0	◆ RFPs Due
10	RFP Evaluation	5	■ RFP Evaluation
11	Designer NOI	0	◆ Designer NOI
12	Designer & CxA 5 Day Appeal Period	5	■ Designer & CxA 5 Day Appeal Period
13	Designer and CxA Contract Execution	5	■ Designer and CxA Contract Execution
14	Design Kick-Off Meeting	0	◆ Design Kick-Off Meeting
15	35% Design	20	■ 35% Design
16	35% Design Contractibility Review	5	■ 35% Design Contractibility Review
17	35% Budget Development	5	■ 35% Budget Development
18	35% Submittal	0	◆ 35% Submittal
19	35% Design Review	5	■ 35% Design Review
20	35% Design Meeting	0	◆ 35% Design Meeting
21	50% Design	15	■ 50% Design
22	VA Submittal & Request for Comment Form	0	◆ VA Submittal & Request for Comment Form
23	VA Approval	30	■ VA Approval
24	50% Design Contractibility Review	5	■ 50% Design Contractibility Review
25	50% Budget Development	5	■ 50% Budget Development
26	50% Submittal	0	◆ 50% Submittal
27	50% Review	5	■ 50% Review
28	State SHPO Submittal	0	◆ State SHPO Submittal
29	State SHPO Resposne	30	■ State SHPO Resposne
30	Design Development Review Mtg.	0	◆ Design Development Review Mtg.
31	75% CD Development	10	■ 75% CD Development

Actual Work

Remaining Work


Critical Remainin...

◆ Milestone

Page 1 of 3

TASK filters: Comments, Hide Done Activities.

© Oracle Corporation

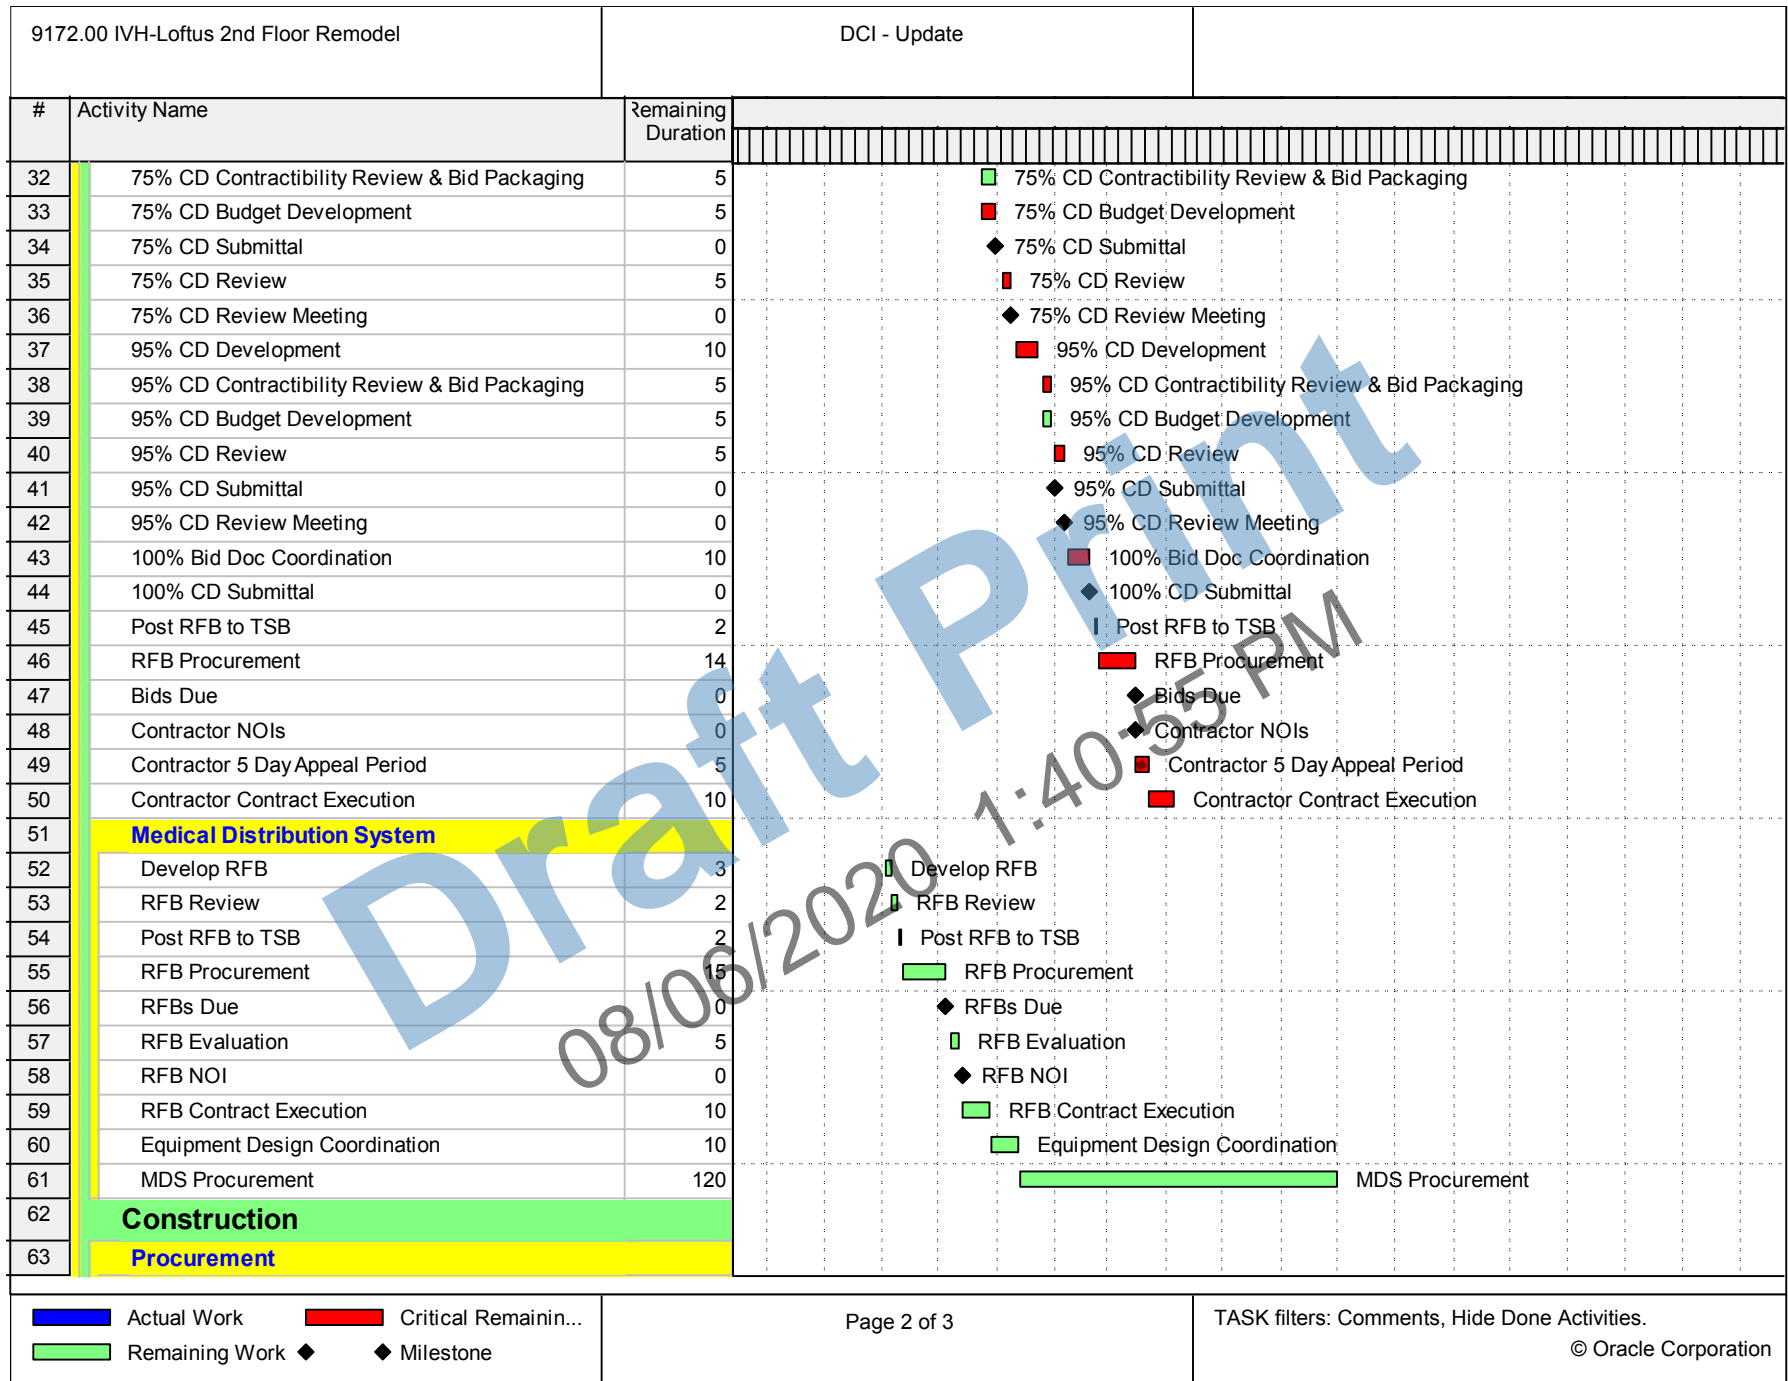

9172.00 IVH-Loftus 2nd Floor Remodel			DCI - Update		
#	Activity Name	Remaining Duration			
64	Submittals and Material Procurement	80	Submittals and Material Procurement		
65	Demo				
66	Demolition	98	Demolition		
67	Buildback				
68	Construction	151	Construction		
69	Closeout				
70	Closeout	91	Closeout		

Draft Print
08/06/2020 1:40:55 PM

■ Actual Work ■ Critical Remainin...
■ Remaining Work ◆ Milestone
